


Henry-2/2DW1ST1 Time versus Depth Curve

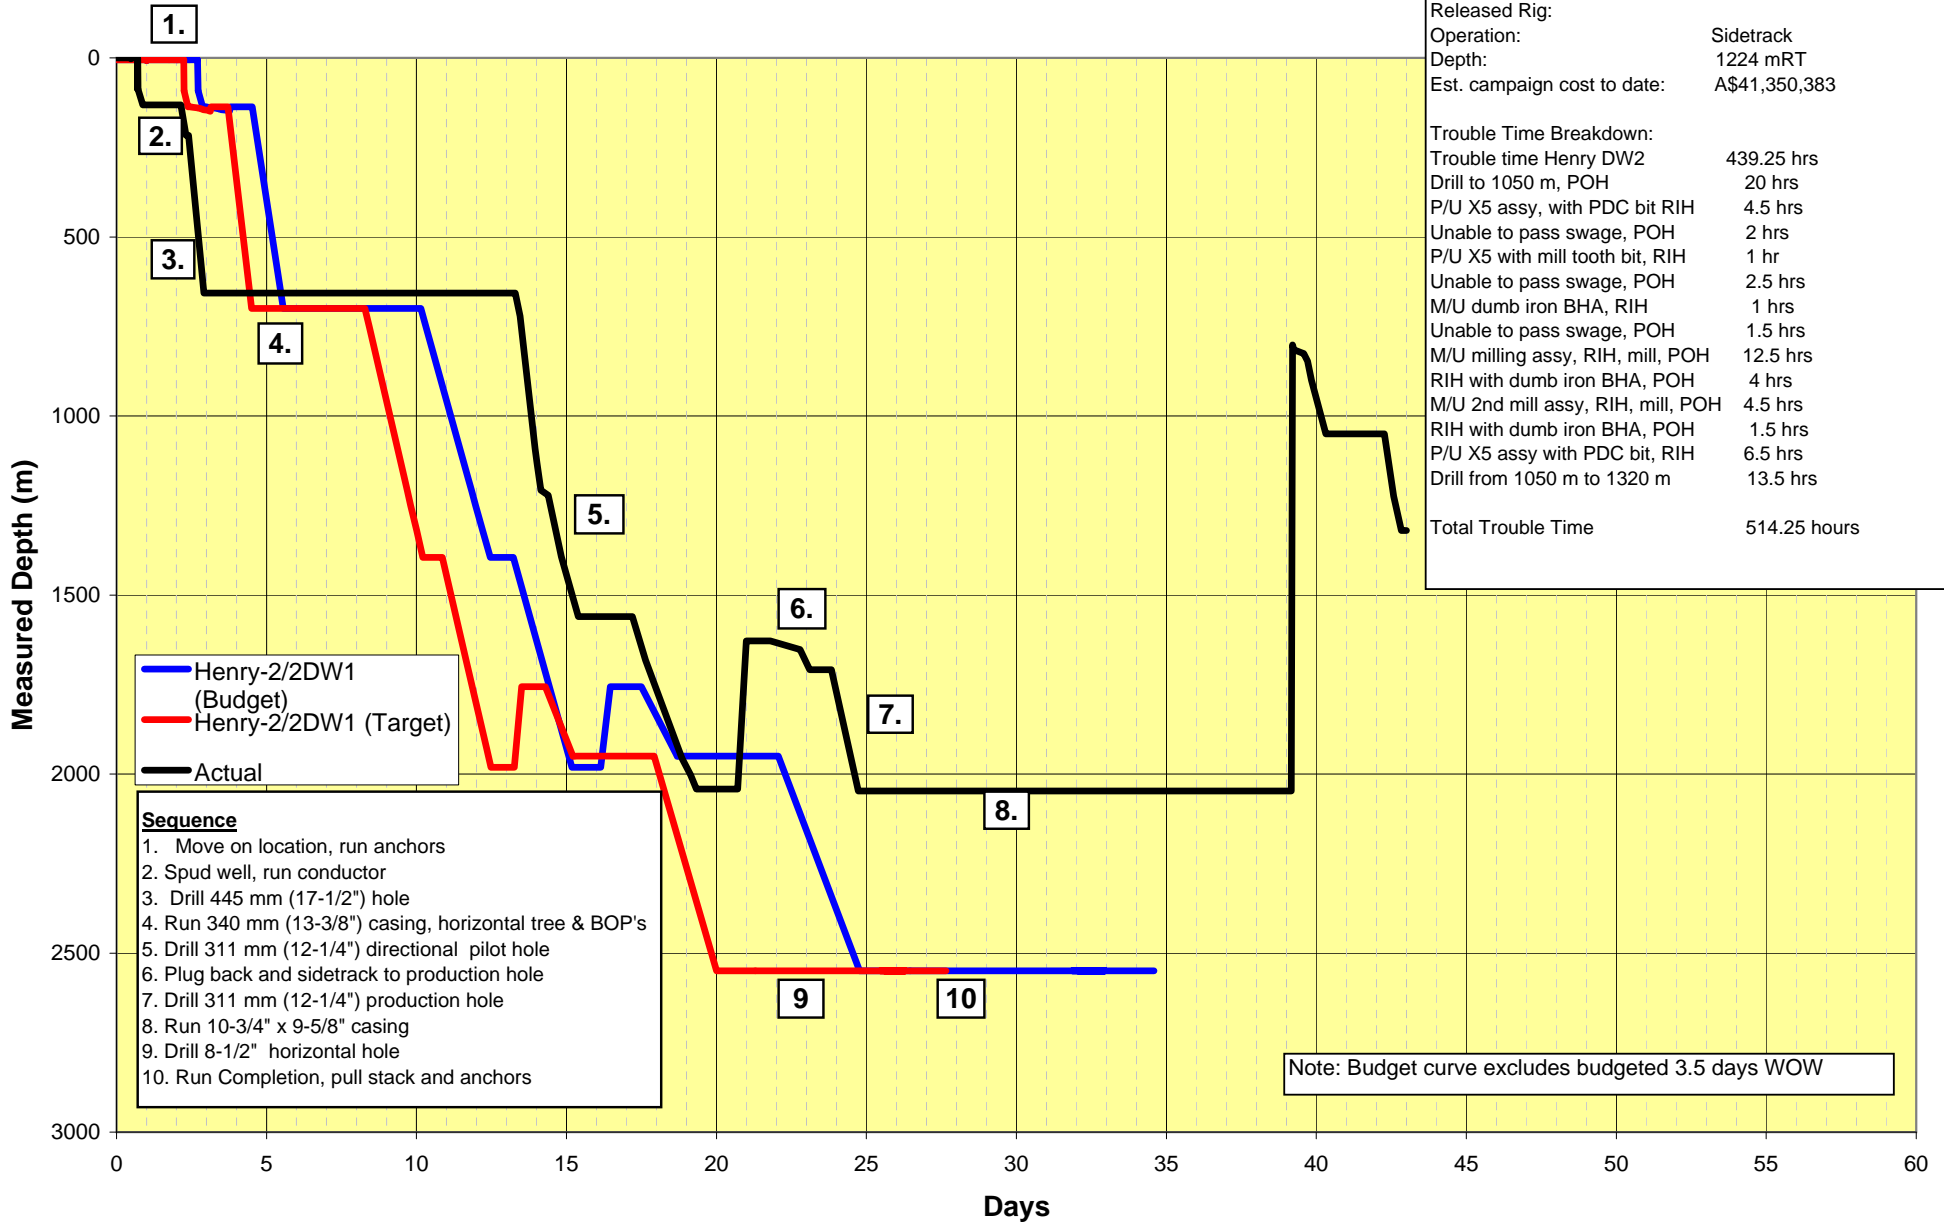

Henry-2/2DW1ST1 Mon 6th October @ 0600hrs	
Commenced Well:	24 August 2008 @ 12:30 hrs
Spud Well:	25 August 2008 @ 03:15 hrs
Released Rig:	
Operation:	Sidetrack
Depth:	1224 mRT
Est. campaign cost to date:	A\$41,350,383
Trouble Time Breakdown:	
Trouble time Henry DW2	439.25 hrs
Drill to 1050 m, POH	20 hrs
P/U X5 assy, with PDC bit RIH	4.5 hrs
Unable to pass swage, POH	2 hrs
P/U X5 with mill tooth bit, RIH	1 hr
Unable to pass swage, POH	2.5 hrs
M/U dumb iron BHA, RIH	1 hrs
Unable to pass swage, POH	1.5 hrs
M/U milling assy, RIH, mill, POH	12.5 hrs
RIH with dumb iron BHA, POH	4 hrs
M/U 2nd mill assy, RIH, mill, POH	4.5 hrs
RIH with dumb iron BHA, POH	1.5 hrs
P/U X5 assy with PDC bit, RIH	6.5 hrs
Drill from 1050 m to 1320 m	13.5 hrs
Total Trouble Time	514.25 hours
