Enclosure 6b

Schlumberger

Cement Bond - Variable Density Log CBL-VDL-GR-CCL Iona #2 1:500

DEPT. NAT. RES & ENV
PE600783

STATE	Victoria
FIELD	Iona
LOCATION	Iona 93-01
WELL	Iona #2
COMPANY	GFE Resources Ltd.

COMPANY	GFE Resources Ltd.				
WELL	Iona #2				
FIELD	Iona				
STATE	Victoria		RIG	Century Rig-11	
LOCATION	Iona 93-01 VP 248.2	038 34'30.989" S 143 02'01.585" E			Other Services: 4 1/2" HSD JB PPS
API SERIAL NO.		SECT.	TWP.	RANGE	

Permanent Datum	MSL	Elev. 0.0 M	Elev.: K.B.134.3 M
Log Measured From	KB	134.3 M above Perm. Datum	D.F.134.0 M
Drilling Measured From	KB		G.L.130.0 M

Date	03-03-1994			
Run No.	1			
Depth Driller	1435.0 M			
Depth Logger (Schl.)	1437.0 M			
Btm. Log Interval	1435.0 M			
Top Log Interval	855.0 M			
Type Fluid in Hole	Brine			
Salinity NaCl				
Density	9.10 LB/G			
Fluid Level				
Max. Rec. Temp.				
Deviation	26 DEG			
Logger on Bottom	06:27 03-03-1994			
Equip. | Location	8386	QEA		
Recorded By	M.Wilson.			
Witnessed By	Dean Grant			
BOREHOLE RECORD				
Bit Size	12 1/4"	8 1/2"		
Depth	640.0 M	1650.0 M		
CASING & TUBING RECORD				
Size	9 5/8"	7"		
Weight	36.0000 LB/F	26.0000 LB/F		
Casing Top-Driller	0.0 M	0.0 M		
Casing Top-Logger				
Casing Shoe-Driller	637.0 M	1444.0 M		
Casing-Logger	636.0 M			

The well name, location and borehole reference data were furnished by the customer.

All interpretations are opinions based on inferences from electrical or other measurements and we cannot, and do not guarantee the accuracy or correctness of any interpretations, and we shall not, except in the case of gross or willful negligence on our part, be liable or responsible for any loss, costs, damages or expenses incurred or sustained by anyone resulting from any interpretations made by any of our officers, agents or employees. These interpretations are also subject to Clause 4 of our General Terms and Conditions as set out in our current Price Schedule.

Run No.	1
Service Order No.	
Logging Speed	900.0 F/HR
EQUIPMENT DATA	
Tool Number 1	TCM-AB 16
Tool Number 2	STM-CA 208
Tool Number 3	WDM-AB 836
Tool Number 4	TCC-B 555
Tool Number 5	SGC-SA 1279
Tool Number 6	SLS-CB 298
Tool Number 7	SLR-CB 259
Tool Number 8	SDC-CB 227
Tool Number 9	CAL-YA 576
Tool Number 10	
Tool Number 11	
Tool Number 12	

REMARKS:

Log correlated to DLL-MSFL-GR, Run #1. (25-Feb-94)
Tool run centralised with 3 x gemcos.
Cement job finished 03:30 01-03-1994.
Pumped Class g cement with Halad 322.
Recorded waveforms simultaneously with CBL .
Well logged with no surface pressure applied to casing .
Apparent top of cement at 320 m

MAIN LOG 1:500

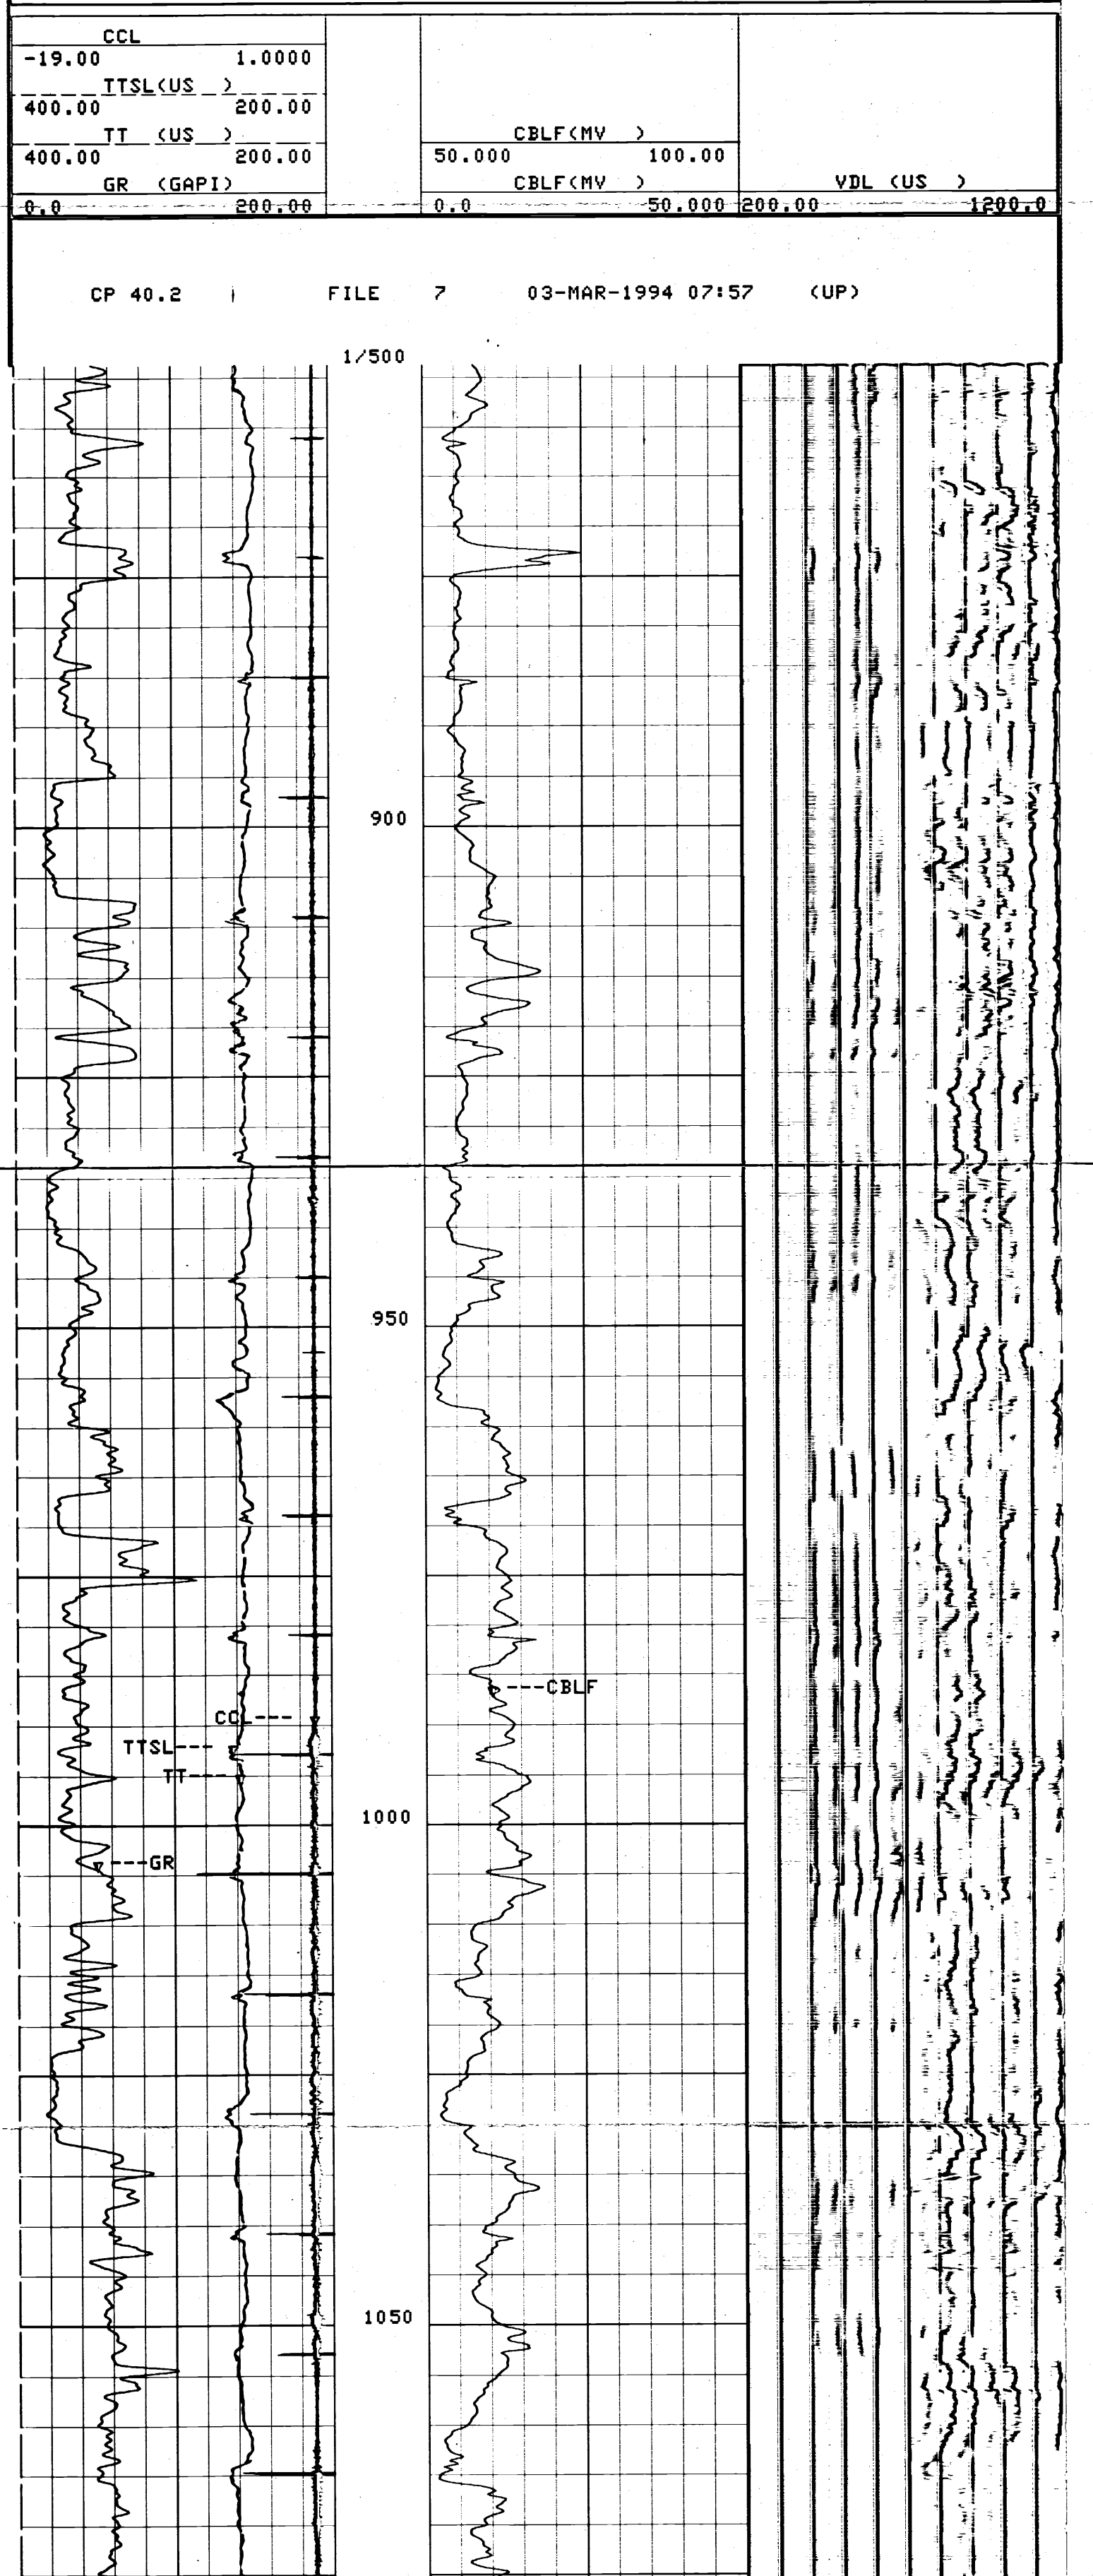

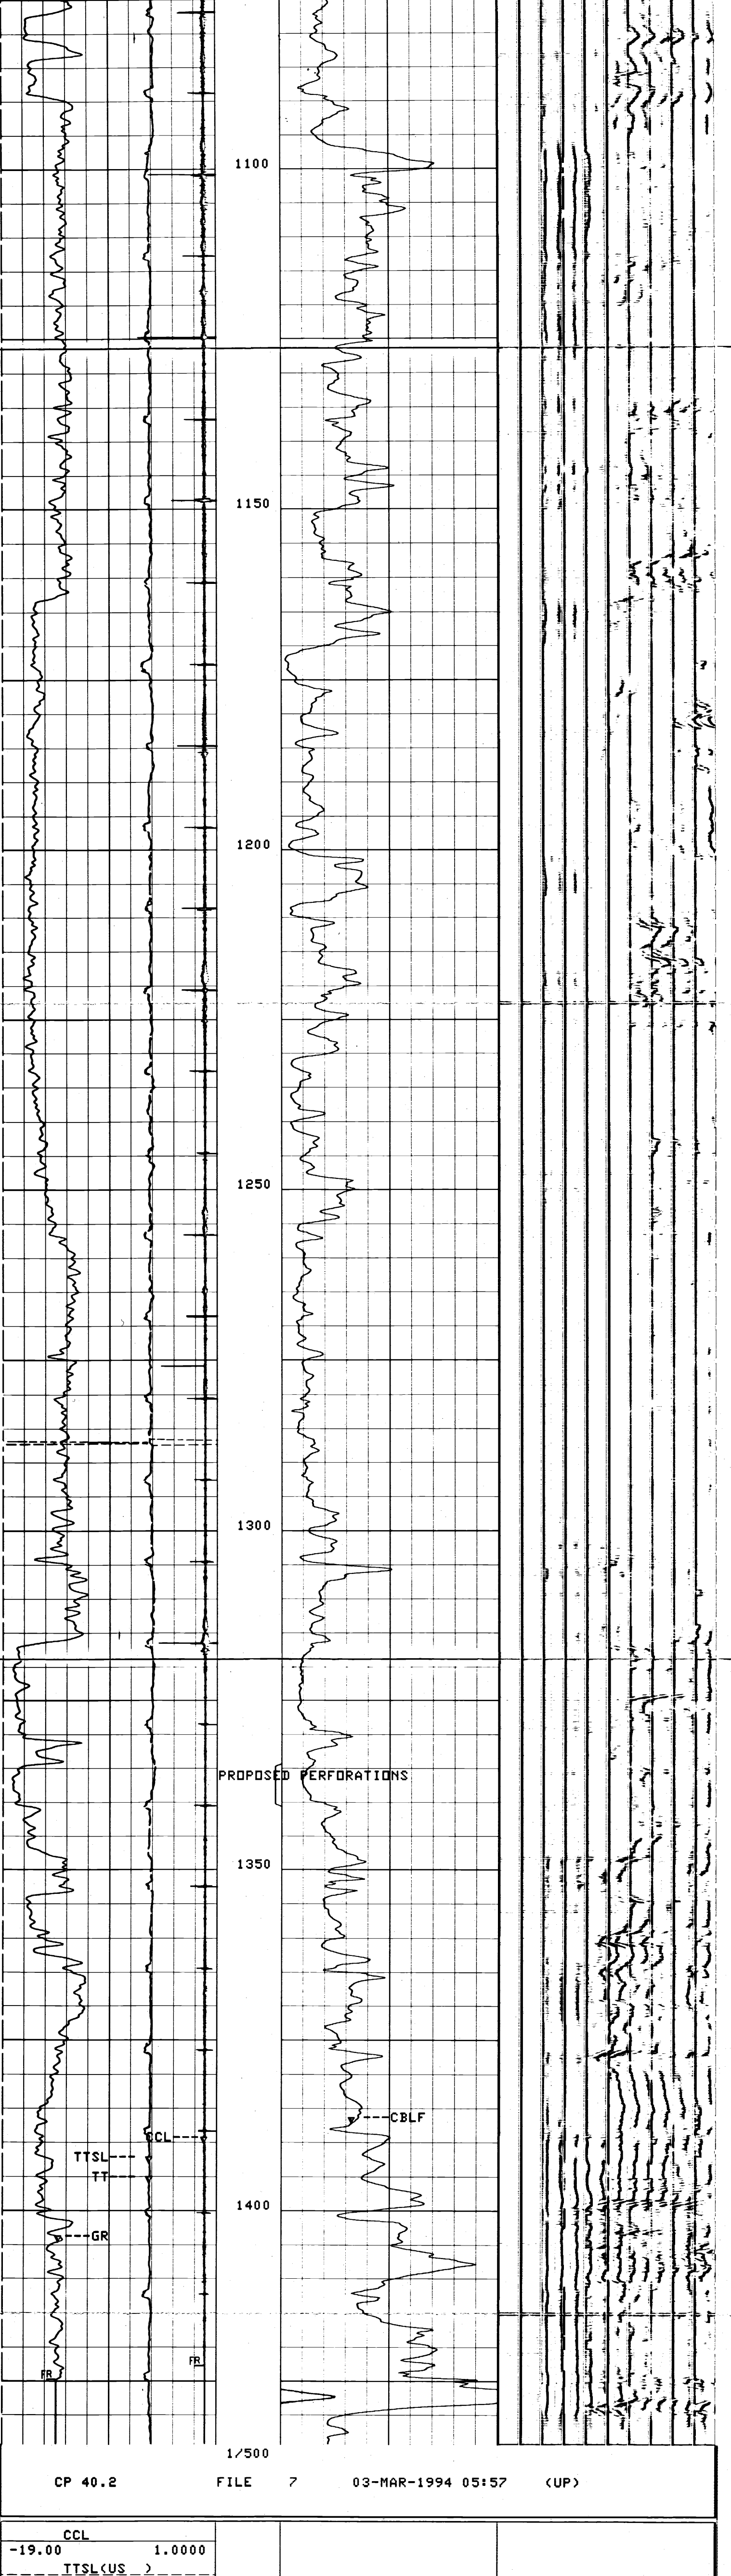

1/500

CP 40.2 FILE 7 03-MAR-1994 05:57 (UP)

CCL -19.00 1.0000 TTSL(US) 400.00 200.00 TT (US) 400.00 200.00 GR (GAPI) 0.0 200.00	CBLF(MV) 50.000 100.00 CBLF(MV) 0.0 50.000	VDL (US) 200.00 1200.0

COMPANY	GFE Resources Ltd.			SCHL. FR	1435.0 M
WELL	Iona #2			SCHL. TD	1437.0 M
				DRLR. TD	1435.0 M
FIELD	Iona			Elev: KB	134.3 M
				DF	134.0 M
STATE	Victoria	**RIG**	Century Rig-11	GL	130.0 M

Schlumberger

Cement Bond - Variable Density Log CBL-VDL-GR-CCL Iona #2 1:500
